

Tel: 07789 032544
Email: andrew.fletcher@wokingham.gov.uk
Date: 8th April 2022
File ref: Greenways Route B Section 2.1



**WOKINGHAM
BOROUGH COUNCIL**

The Occupier / Resident

COMMUNITY, HERITAGE, GREEN
AND BLUE INFRASTRUCTURE

P.O. Box 150

Shute End, Wokingham

Berkshire RG40 1WN

Tel: (0118) 974 6000

Minicom No: (0118) 9746991

Dear Resident

Greenways Route B Section 2.1 (Woosehill Meadows) Construction Works

I am writing to advise you that the Council will shortly be commencing construction works for the Greenway through Woosehill Meadows, as shown on the attached plans.

The works will commence on **9th May 2022** and the indicative programme of works is detailed below. These works are being undertaken in co-ordination with other works along the Emm Brook currently being planned by the South East Rivers Trust (SERT), to ensure that both schemes do not conflict with each other.

Due to the need to co-ordinate the works, three of the phases that are near to or coincide with the areas where SERT are planning to be working do not yet have expected start dates. This is because we are waiting until SERT have a confirmed schedule of works before the date can be agreed with our contractors.

Phase number	Description	Nature of works	Indicative start date
1	North of riverside walk from Dragonfly Bridge northwards	Construction of approx. 150m of path	9 th May 2022
2	South of SERT works towards Kingfisher bridge	Construction of approx. 150m of path	31 st May 2022
3	Continuation of path to link with Kingfisher bridge	Construction of approx. 260m of path	21 st June 2022
4	East from Heron Road to link with Smiths Walk	Construction of approx. 360m of path	13 th July 2022
5	South from underpass to the culvert/location of new bridge	Widening and construction of approx. 170m of path	To be confirmed



6	Culvert and section of used route through woods	Replacement of bridge and small section of path to link to Phase 1	To be confirmed
7	South from Riverside Walk path	Construction of approx. 130m of path	To be confirmed

Please note all the dates listed above are indicative and may need to be revised depending on the weather conditions and the progress of the works.

We will be endeavouring to ensure that alternative routes are provided for public access whilst the construction works are being undertaken. Please be advised that some works, such as the removal of the northern culvert and replacement with a bridge, will require a larger closure and diversion of route.

For your information I have also included on the map the planned location of compound areas that will be required to facilitate the works.

Further information about the Greenway, including design drawings and specifications, can be found in the Greenway webpages at <https://www.wokingham.gov.uk/major-developments/greenways-programme/>


If you have any questions at all or would like to discuss this further, please do not hesitate to contact me using my details above, or email greenways@wokingham.gov.uk

Yours sincerely,



Andrew Fletcher
Green Infrastructure Manager

GREENWAYS ROUTE B SECTION 2.1 CONSTRUCTION PHASES

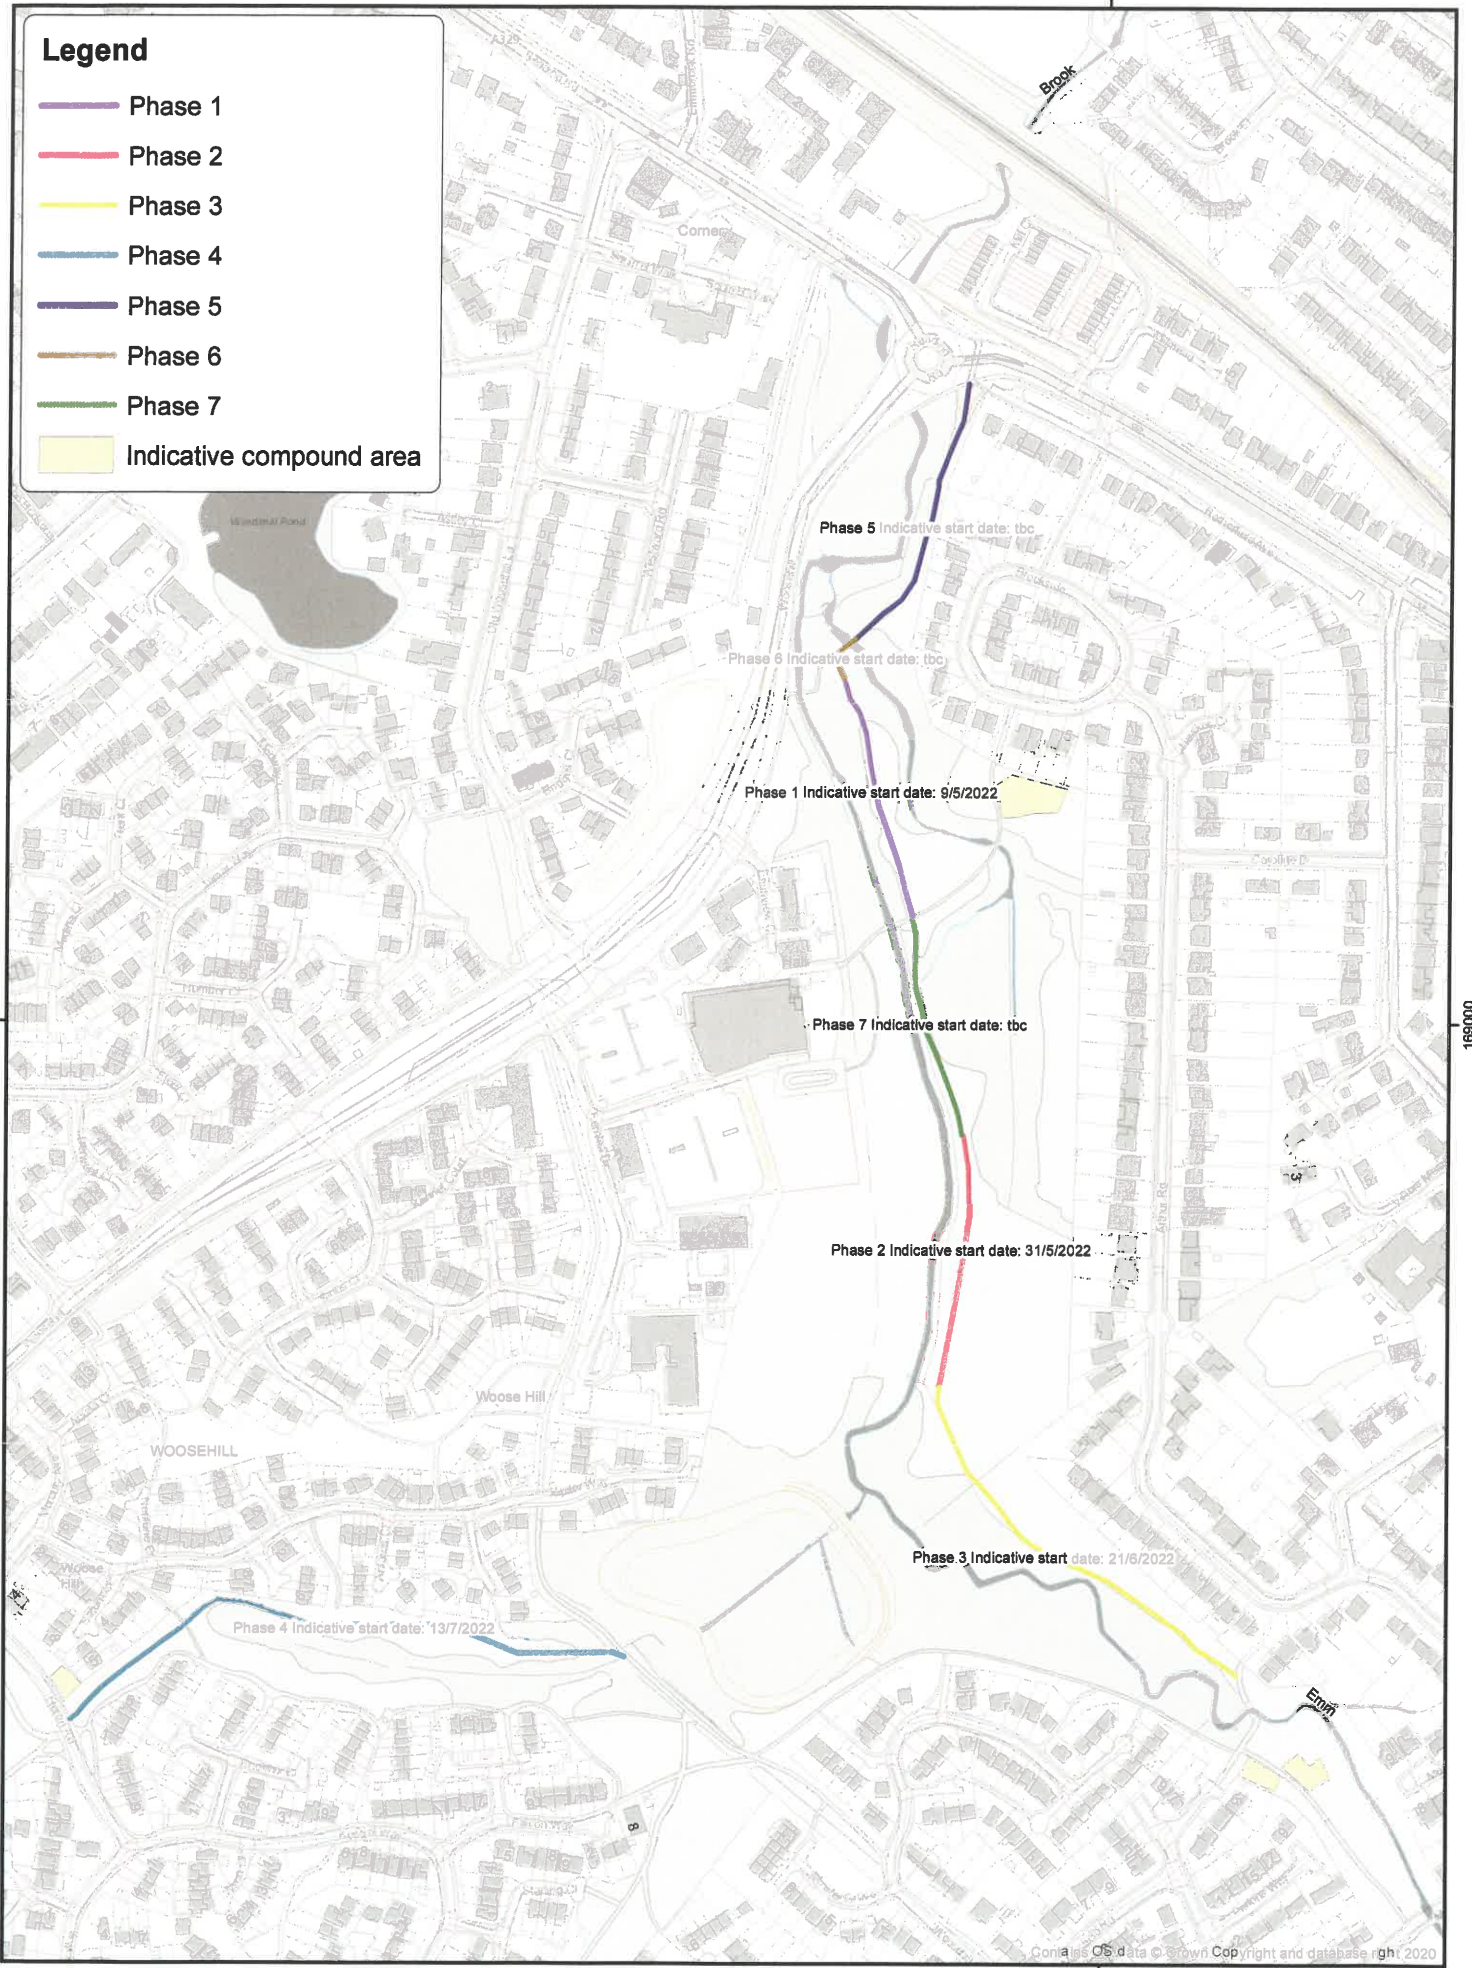

Scale 1:3,100

